





Pilot Off Grid Implementation & Rollouts at Long Loyang Clinic

updated as of Friday, May 29, 2020

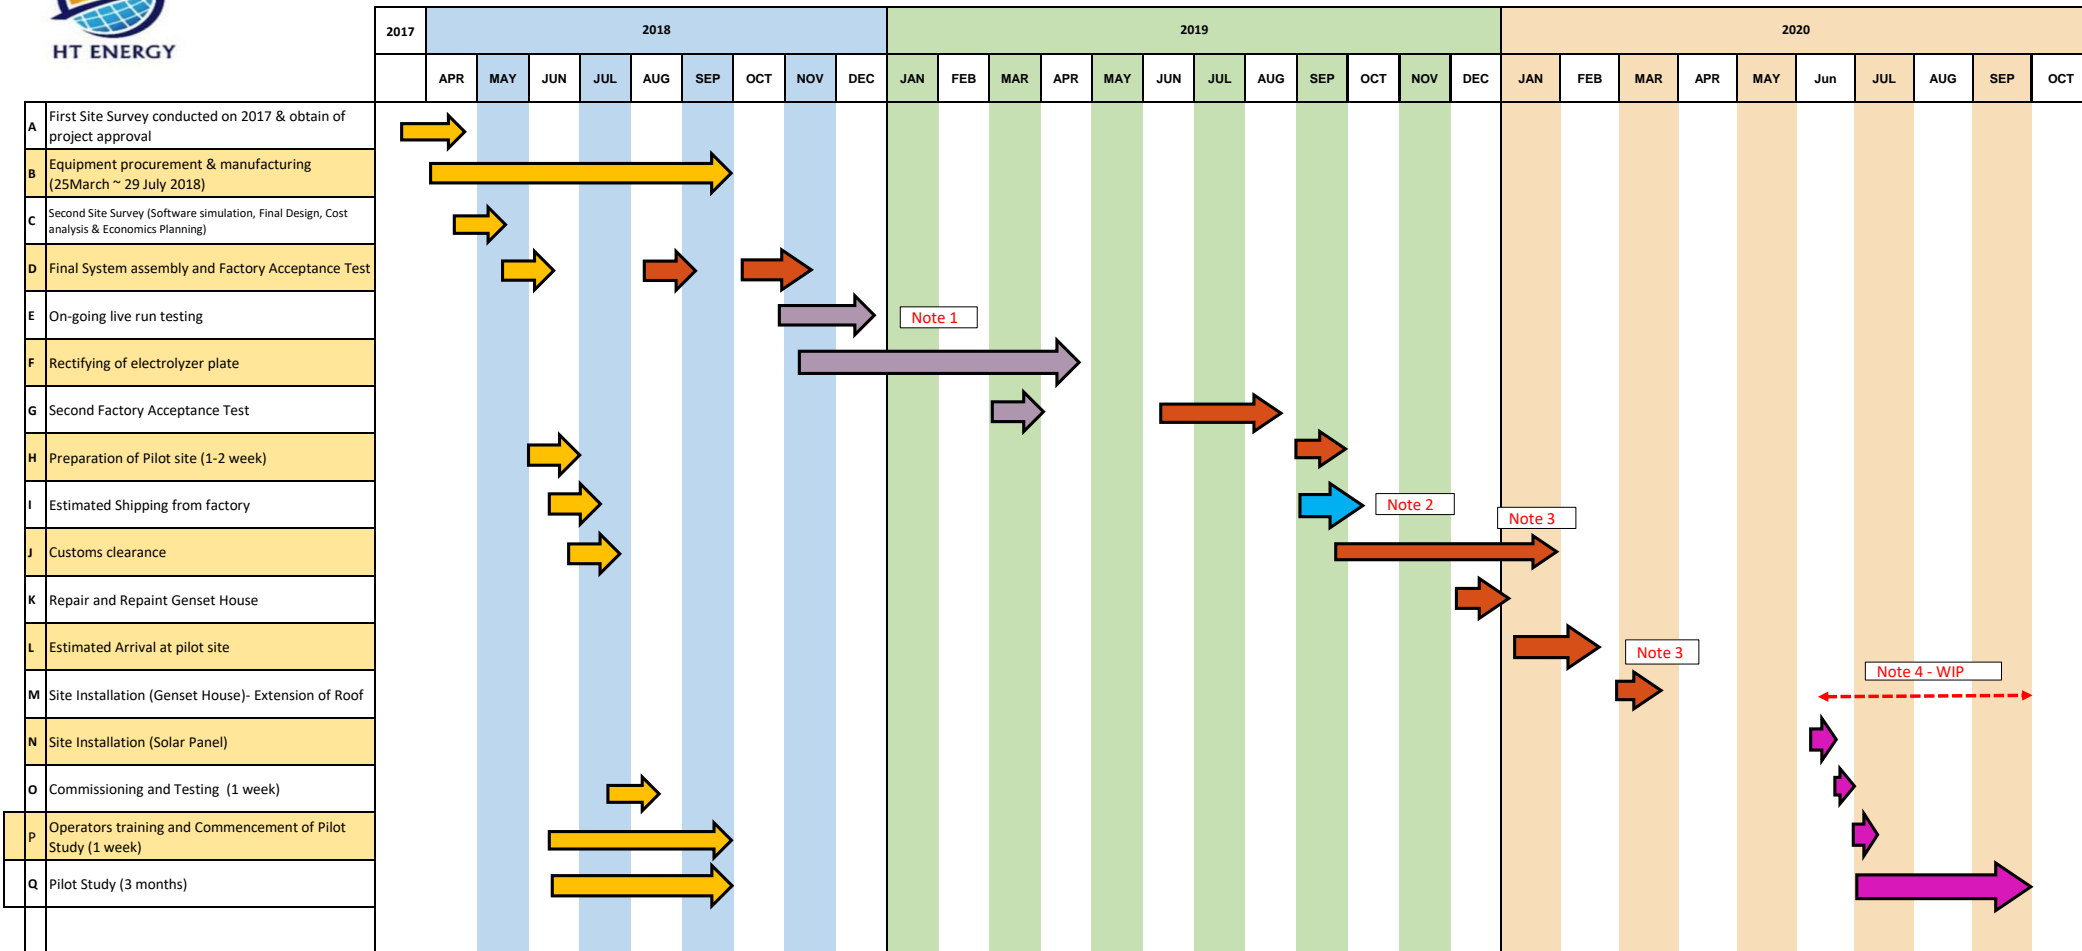

Note 1 - Mid April 2019 to 10 May 2019 - Modification of module enclosure to break up large cabinet into 2 smaller cabinets in order to facilitate smooth transportation at site
- May 2019 to June 2019 - Functional tests & endurance test (to simulate 10 hour daily continuous on-site operation)

Note 2 a) 1st Shipment (Power Module) arrived Miri Port on the 2 Oct 2019

Note 3 - a) Genset House - Paintwork and Repairs -5- 9 Dec 2019
b) custom clearance 30 January 2020
c) Estimate Arrival at Long Loyang - 5 - 7 February 2020 (4-6 trips)
d) Installation of roof extension - 8 - 15 March 2020

Note 4 - WIP
a) Installation solar panel and wiring connection - mid June 2020 (depends on weather), require approximately 10 days
b) Testing and commissioning - 1 week
c) Opeartor Trailing & Commencement of pilot study - 1 week
d) Pilot study - 3 months (Jul - Sep)
