




Pilot Off Grid Implementation & Rollouts at Long Loyang Clinic

updated as of 22-June-2019

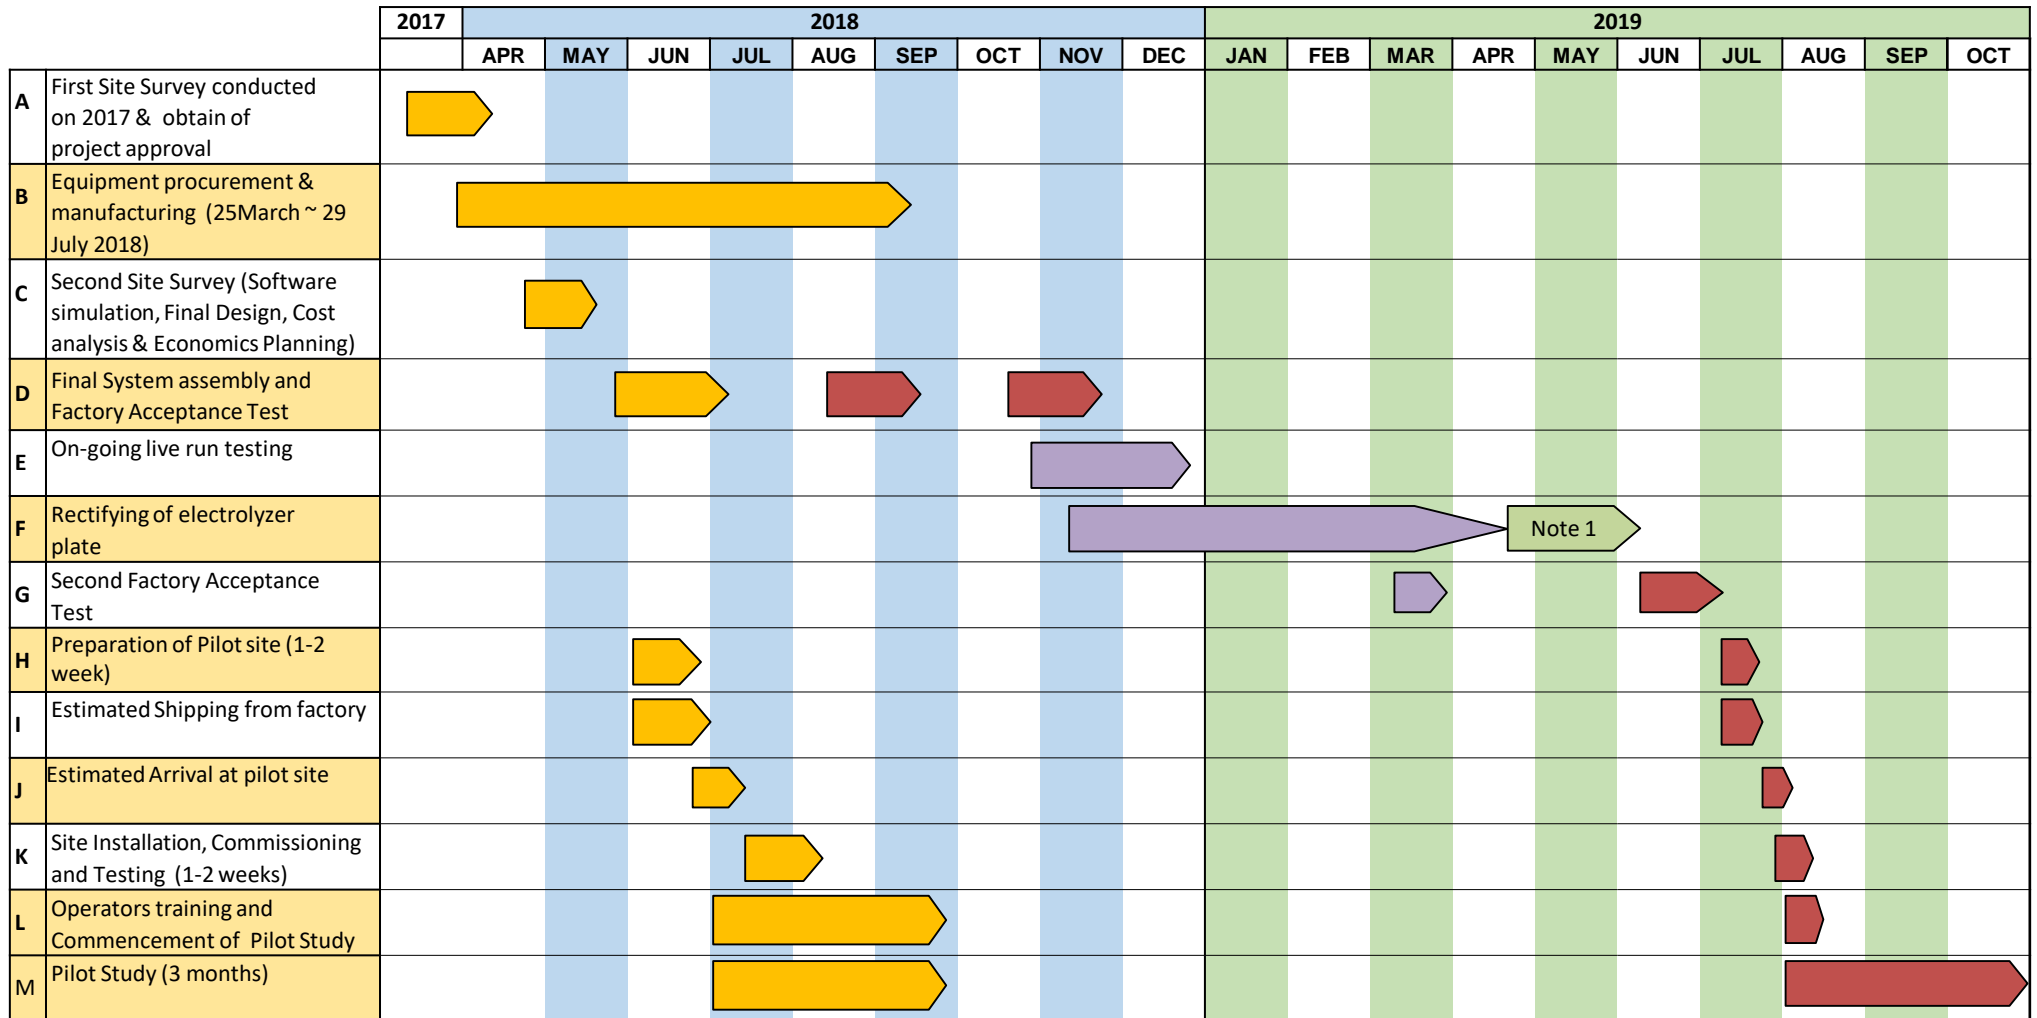

Initial Plan

New Scope

Plan Delay

Improvement work

Note 1 - Mid April 2019 to 10 May 2019 - Modification of module enclosure to break up large cabinet into 2 smaller cabinets in order to facilitate smooth transportation at site
 - May 2019 to June 2019 - Functional tests & endurance test (to simulate 10 hour daily continuous on-site operation)
