




ANG Huizhou Luofushan – design impression

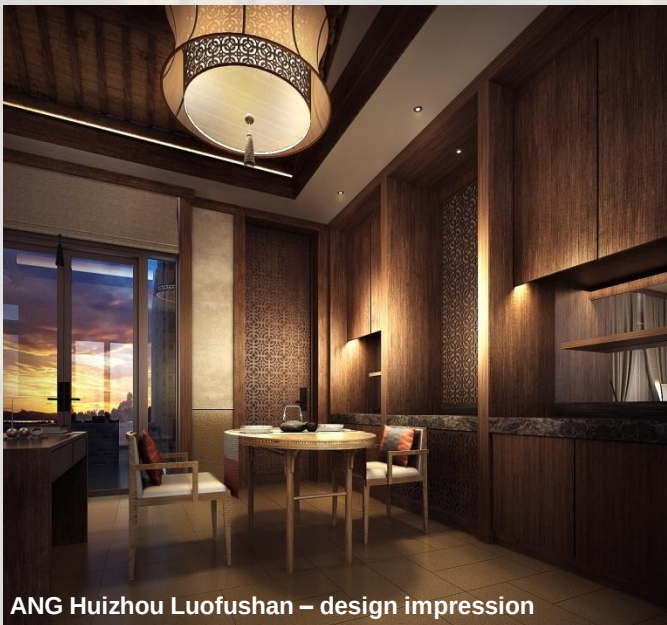

ANG Huizhou Luofushan – design impression

Banyan Tree Holdings Limited

1Q14 Project Progress Report

DISCLAIMER

This document is provided to you for information only and should not be relied on or used as a basis for making any specific investment, business or commercial decision. No representation or warranty, expressed or implied, is made as to, and no reliance should be placed on, the information or opinions contained herein. This document does not constitute and should not be construed as, any offer or solicitation for the subscription, purchase or sale of any securities of Banyan Tree Holdings Limited ("Banyan Tree"). Nothing in this document should be construed as a recommendation regarding the securities of Banyan Tree.

Certain statements in this document may constitute "forward-looking statements", including statements regarding, amongst other things, Banyan Tree's business and growth strategy. These statements reflect Banyan Tree's expectations and are subject to risks and uncertainties that may cause actual results to differ materially and may adversely affect the outcome and financial effects of the plans described herein. You are cautioned not to rely on such forward-looking statements. Banyan Tree disclaims any obligation to update their view of such risks and uncertainties or to publicly announce the result of any revisions to the forward-looking statements made herein, except where they would be required to do so under applicable law.

Banyan Tree is under no obligation to keep current the information contained in this document and any opinions expressed in it are subject to change without notice. None of Banyan Tree or any of its affiliates, advisers or representatives shall have any liability whatsoever for any loss whatsoever arising from any use of this document or its contents, or otherwise arising in connection with this document (whether direct, indirect, consequential or other). This document is not intended to provide professional advice and should not be relied upon in that regard. Prospective investors should consult their tax, legal, accounting or other advisers.

The information in this document is given in confidence and reproduction of this document, in whole or in part, or disclosure of any of its contents, without prior consent of Banyan Tree, is prohibited. This document remains the property of Banyan Tree and on request must be returned and any copies destroyed.



AGENDA

1. Executive Brief

2. Project Completion Schedule



Executive Brief

The purpose of this quarterly report is to update our shareholders on the progress of new projects targeted to open within the next 24 months from now. The current target completion/opening of these resorts and progress status is compared to the last quarter's announced date.

Summary

- ❖ Angsana Nanjing Tangshan's project completion date has been delayed from 2014 to 2015 as the Owner is in the midst of getting third party investors to finance the next project phase.



PROJECT COMPLETION SCHEDULE

2014

NO	Resorts/Hotels <u>With</u> Minority Equity Interest	Status of Project	Current Completion/ Opening	Progress Status	Third Party Owner Delay	BTH Delay	Remarks
	<u>Banyan Tree</u>						
1.	Yangshuo, Guilin, China	90% Construction	2014		√		Incremental weather has slowed down construction progress.
2.	Huangshan, Anhui, China	70% Construction	2014				

NO	Resorts/Hotels <u>Without</u> Equity Interest	Status of Project	Current Completion/ Opening	Progress Status	Third Party Owner Delay	BTH Delay	Remarks
	<u>Angsana</u>						
1.	Xian Lingtong, Shaanxi, China	90% Construction	2014				

Note: Project Progress Status is compared to the last quarter announced date.

	Progress on track
	On track, but might be delayed (3 to 6 months) pending some issues
	Delayed (more than 6 months), see attached Delayed Project Report

PROJECT COMPLETION SCHEDULE

2015

NO	Resorts/Hotels <u>Without</u> Equity Interest	Status of Project	Current Completion / Opening	Progress Status	Third Party Owner Delay	BTH Delay	Remarks
	<u>Banyan Tree</u>						
1.	Tamouda Bay, Tetouan, Morocco	55% Construction	2015				
2.	Anji, Zhejiang, China	Design Development	2015				
3.	Tianjin Yangliuqing, Tianjin, China	15% Construction	2015				
4.	Dali, Yunnan, China	Design Development	2015				
5.	Jiuzhaigou, Sichuan, China	40% Construction	2015				

Note: Project Progress Status is compared to the last quarter announced date.

	Progress on track
	On track, but might be delayed (3 to 6 months) pending some issues
	Delayed (more than 6 months), see attached Delayed Project Report

PROJECT COMPLETION SCHEDULE

2015

NO	Resorts/Hotels <u>Without</u> Equity Interest	Status of Project	Current Completion / Opening	Progress Status	Third Party Owner Delay	BTH Delay	Remarks
	<u>Angsana</u>						
1.	Marbella, Spain	25% Construction	2015				
2.	Langfang, Hebei, China	Schematic Design	2015				
3.	Huizhou Luofushan, Guangdong, China	Mock Up Construction	2015				
4.	Chongqing Beibei, Chongqing, China	10% Construction	2015				
5.	Nanjing Tangshan, Jiangsu, China	50% Construction	2015		√		Owner is in the midst of getting third party investors to finance the next project phase.

Note: Project Progress Status is compared to the last quarter announced date.

	Progress on track
	On track, but might be delayed (3 to 6 months) pending some issues
	Delayed (more than 6 months), see attached Delayed Project Report

PROJECT COMPLETION SCHEDULE

2016

NO	Resorts/Hotels <u>Without</u> Equity Interest	Status of Project	Current Completion / Opening	Progress Status	Third Party Owner Delay	BTH Delay	Remarks
	<u>Banyan Tree</u>						
1.	Goa, India	Schematic Design	2016				
2.	Batu Bay, Inner Mongolia, China	Schematic Design	2016				
3.	Yangcheng Lake, Jiangsu, China	Concept Design	2016				
4.	Janabiya, Manama, Kingdom of Bahrain	Concept Design	2016				
5.	Emeishan, Sichuan, China	Concept Design	2016				

Note: Project Progress Status is compared to the last quarter announced date.

	Progress on track
	On track, but might be delayed (3 to 6 months) pending some issues
	Delayed (more than 6 months), see attached Delayed Project Report

PROJECT COMPLETION SCHEDULE

2016


NO	Resorts/Hotels <u>Without</u> Equity Interest	Status of Project	Current Completion / Opening	Progress Status	Third Party Owner Delay	BTH Delay	Remarks
	<u>Angsana</u>						
1.	Penon Del Lobo, La Herradura, Spain	Schematic Design	2016				
2.	Kunming North, Yunnan, China	10% Construction	2016				
3.	Qingcheng Shan, Chengdu, China	Concept Design	2016				
4.	Fuzhou Changle, Fujian, China	Concept Design	2016				
5.	Teluk Bahang, Penang, Malaysia	Concept Design	2016				

Note: Project Progress Status is compared to the last quarter announced date.

	Progress on track
	On track, but might be delayed (3 to 6 months) pending some issues
	Delayed (more than 6 months), see attached Delayed Project Report



ANG Huizhou Luofushan – design impression

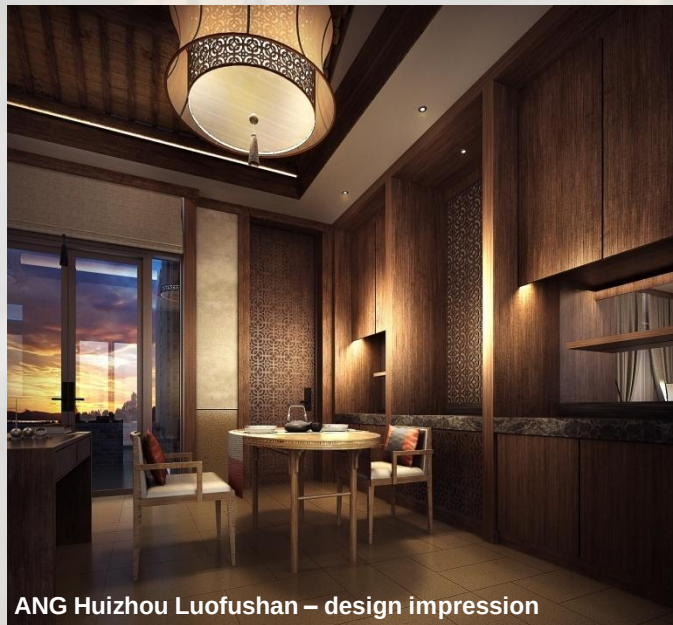

ANG Huizhou Luofushan – design impression

THANK YOU
